

MBS Road Control Tower

غرفة عمليات طريق الأمير محمد بن سلمان

Curated knowledge base for the Prince Mohammed bin Salman
Road corridor — Jeddah Islamic Port to Al-Masjid Al-Haram,
75 km, 170,000+ vehicles per day.

MBS Road Control Tower — Knowledge Base

Curated reference for the MBS Road Control Tower Agent. Single source of truth for leadership briefings, agent onboarding, and LLM context.

Corridor: Prince Mohammed bin Salman Road · Jeddah → Makkah · 75 km · 170,000+ vehicles/day
Owner: Saudi Ministry of Municipalities & Housing (MoMAH) **Document version:** 0.1 · synthetic PoC data (Zones 8, 35, 70 only)

Table of contents

#	Section	What's inside
00	Executive Summary	1-page leadership view: corridor, KPIs, Hajj readiness, top risks
01	Corridor Overview	The 75 km road, 3 sub-stretches, 5 phases, the strategic case
02	2027 Targets (KPIs)	All 6 KPIs with current %, target %, weekly trend, status
03	Zones — PoC Detail	Full picture of Zones 8, 35, 70 — findings, budgets, assets, contractors
04	Contractors & Governance	The 10 contractors, why governance is a root cause, joint-room proposal
05	Activity Types & Glossary	Development vs Operational, distortion categories, key terms
06	Questions & Answers	54 bilingual (EN+AR) Q&A pairs grouped by topic
07	Facts Snapshot (JSON)	Machine-readable single source of truth — feeds the LLM

How to use this folder

Audience	Read first
Leadership briefing	00-executive-summary.md
Stakeholder review	01-corridor-overview.md → 02-2027-targets.md → 04-contractors-and-governance.md
Agent / LLM training	06-questions-and-answers.md + 07-facts-snapshot.json
Field / operational team	03-zones.md + 05-activity-types-and-glossary.md

Snapshot at a glance

Metric	Value
Corridor length	75 km
Daily vehicles	170,000+
Zones	75 (1 km each)
Operational phases	5 (15 zones each)
Geographic sub-stretches	3 (Port · Middle · Haram)
Contractors involved	10
2027 KPIs tracked	6
PoC zones with synthetic data	Z8, Z35, Z70
Findings tracked (PoC)	26 (10 Development · 16 Operational)
Q&A pairs in the KB	62 (bilingual EN/AR · incl. vendor performance)

Sources

- **April 2026 report** — *Status of Prince Mohammed bin Salman Road Axis in the Makkah region and proposed remediation actions* (Saudi Ministry of Municipalities & Housing)
- **PoC synthetic data** — generated to demonstrate the platform pending live data integration

Document classification: internal MoMAH briefing material · synthetic PoC data

00 · Executive Summary

For: MoMAH leadership **About:** Status of the Prince Mohammed bin Salman Road Axis (Jeddah → Makkah)

The corridor in one line

A **75 km strategic link** between Jeddah Islamic Port and Al-Masjid Al-Haram, carrying **170,000+ vehicles daily** — the principal road for pilgrims, Umrah travellers, logistics flows, and inter-city commerce.

Why the program exists

The April 2026 ministerial report identified **four root-cause challenges** along the corridor:

- 1. **No single supervising authority** — work is split across 7 contractors with overlapping mandates
- 2. **Visual distortion (تشوه بصري)** — slums, illegal workshops, code-violating fuel stations, damaged ad boards, deteriorated asphalt
- 3. **Weak infrastructure** — barriers, bridge perimeters, asphalt, inspection-point quality
- 4. **Unused economic opportunity** — vacant municipal land, untapped advertising/concession potential

2027 targets — current status

KPI	Target	Today	Weekly Δ	On track?
Road maintenance coverage	100%	38%	+4.2%	✓
Buildings compliant with urban codes	70%	22%	+2.1%	×
Illegal workshops & yards cleared	100%	41%	+6.0%	× (but strongest weekly gain)
Damaged concrete barriers repaired	90%	53%	+5.3%	✓
Condemned buildings demolished	100%	28%	+3.7%	×
Greenery & median planting added	100%	19%	+1.4%	× (slowest)

Hajj readiness

- **Next Hajj target date:** 2027-05-25
- Overall corridor is **tracking but behind the ramp** on 4 of 6 KPIs
- **Highest priority zone:** Z70 (Prince Nayef → Holy Mosque approach) — direct pilgrim entry

Top risks (synthesized from PoC findings)

1. **Greenery uplift is the slowest-moving KPI** (+1.4% / wk vs. 100% target). Without acceleration, the visual welcome experience for pilgrims will lag.
2. **Building compliance** is at 22% of a 70% target with only +2.1% weekly momentum.
3. **Repeat-offender pattern:** workshops in Z8 have been flagged for the 3rd time in the quarter (oil spills). Operational handling is no longer sufficient — needs a development-level intervention (licensing review or demolition).
4. **Inter-contractor hand-offs:** blocked items concentrated in items requiring coordination between RGA (roads) and the municipalities (HCM/JM).

Proposed governance fix

An **independent program led by MoMAH** that combines the Holy Capital Municipality (Makkah) and Jeddah Municipality in a **joint working room** with formal authority over findings remediation and stakeholder coordination.

→ Continue to [01 · Corridor Overview](#)

01 · Corridor Overview

The road


Official name	Prince Mohammed bin Salman Road Axis (محور طريق الأمير محمد بن سلمان)
Region	Makkah, Saudi Arabia
Length	75 km
Endpoints	Jeddah Islamic Port → Al-Masjid Al-Haram
Daily traffic	170,000+ vehicles
Primary user mix	Pilgrims & Umrah travellers, inter-city commuters, logistics, recreational, diplomatic

Strategic importance

The corridor is the **principal vehicle link between Jeddah and Makkah** and the main road by which pilgrims, Umrah travellers, and diplomatic guests reach Al-Masjid Al-Haram. It is also a critical logistics spine from the Islamic Port — so visual quality, traffic flow, and safety along it carry **outsized symbolic and operational weight** for the Kingdom.

The 3 geographic sub-stretches

The corridor splits naturally into three contexts:

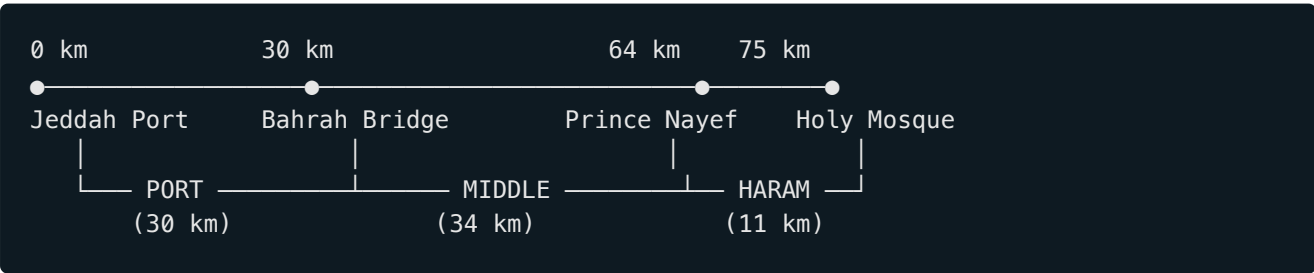

ID	Stretch	Length	Character
port	Port → Bahrah	0 – 30 km	Logistics & port traffic, workshops, mechanic yards, heavy vehicles
middle	Bahrah → Prince Nayef	30 – 64 km	Inter-city movement, fuel stations, ad boards, slum pockets
haram	Prince Nayef → Holy Mosque	64 – 75 km	Pilgrim approach — highest leadership scrutiny, visual welcome critical

The 5 operational phases × 15 zones

Independent of geography, the corridor is divided into **75 zones of 1 km each**, grouped into **5 rollout phases of 15 zones**. Every zone carries **both** a phase (when work is scheduled) and a sub-stretch (its geographic character).

Phase	Zones	Notes
1	Z1 – Z15	Port-side launch (starts logistics belt)
2	Z16 – Z30	Crosses into Bahrah
3	Z31 – Z45	Middle stretch — slum + ad-board concentration
4	Z46 – Z60	Toward Prince Nayef
5	Z61 – Z75	Haram approach — Hajj-readiness priority

Distortion density (3-band classification)

Each zone is rated on a 3-band scale of visible distortion concentration:

Band	Color (UI)	Meaning
Low	 Green	Few or no distortion items; mostly compliant
Medium	 Orange	Some clusters of distortion; needs scheduled attention
High	 Red	Dense clusters; priority for development / remediation

Concentration belts (high density): workshops around Z8–Z14, slums and ad-boards around Z33–Z40, fuel-station & barrier issues around Z50–Z56, pilgrim-approach issues around Z66–Z72.

PoC scope

Synthetic data is currently populated for **three zones — one per sub-stretch**:

- **Z8** — Port stretch · Phase 1 · workshops & barriers
- **Z35** — Middle stretch · Phase 3 · slums, ad boards, fuel stations
- **Z70** — Haram approach · Phase 5 · bridge perimeter & inspection point

→ Continue to [02 · 2027 Targets \(KPIs\)](#)

02 · 2027 Targets (KPIs)

Source: Slide 11 of the April 2026 MoMAH report — *Outcomes targeted by end of 2027* **Numbers below:** synthetic PoC values reflecting the kind of leadership KPI panel that will be hydrated with live operational data.

Snapshot

#	KPI	Target	Today	Weekly Δ	On track?
1	Road maintenance coverage	100%	38%	+4.2%	✓
2	Buildings compliant with urban codes	70%	22%	+2.1%	×
3	Illegal workshops & yards cleared	100%	41%	+6.0%	×
4	Damaged concrete barriers repaired	90%	53%	+5.3%	✓
5	Condemned buildings demolished	100%	28%	+3.7%	×
6	Greenery & median planting added	100%	19%	+1.4%	×

On-track rule: current % is at least 50% of its target % at the current point in the program.

1. Road maintenance coverage

Target: 100% of the corridor under active maintenance coverage by end of 2027. **Today:** 38% · trending **+4.2% / week**

Maintenance coverage = asphalt overlay, drainage, signage, line-painting, joint-sealing across the 75 km. This is the **flagship 100%-by-2027 commitment** and the most visible signal that the corridor is being looked after.

2. Buildings compliant with urban codes

Target: 70% of corridor-facing buildings compliant with the **unified urban code** by end of 2027. **Today:** 22% · trending **+2.1% / week**

Compliance covers façade design, height, signage size, setbacks, materials. Lifting this number requires sustained pressure on building owners — currently the **slowest-moving "code" KPI**.

3. Illegal workshops & yards cleared

Target: 100% of unlicensed mechanic / bodywork / warehouse operations cleared from the right-of-way and adjacent strip by end of 2027. **Today:** 41% · trending **+6.0% / week** — the **strongest weekly delta**.

Driven mostly by Z8-style port-stretch clearances. The trend suggests this KPI hits target ahead of plan if pace is sustained.

4. Damaged concrete barriers repaired

Target: 90% of damaged median and edge barriers repaired or replaced by end of 2027. **Today:** 53% · trending **+5.3% / week** — **the leading on-track indicator** (highest ratio of current to target).

5. Condemned buildings demolished

Target: 100% of buildings with cancelled title deeds (مباني ملغاة صكوكها) demolished by end of 2027. **Today:** 28% · trending **+3.7% / week**

Linked to slum-area work in Z35. Most of the slowdown is process — coordination with social services for resident relocation before demolition.

6. Greenery & median planting added

Target: 100% of the planned greenery & median planting installed by end of 2027. **Today:** 19% · trending **+1.4% / week** — the **furthest behind**.

This is the visual-welcome KPI for pilgrims. The pace needs to roughly double to make Hajj 2027.

What leadership should watch

Watch	Why
Greenery acceleration plan	Lowest weekly velocity (+1.4%) against a 100% target. Without intervention, visual welcome experience for Hajj 2027 will lag.
Compliance enforcement cadence	Building code compliance moves at +2.1%/wk; 70% target may slip.
Demolition coordination	Condemned-building demolitions are bottlenecked by social-services relocation timing.
Workshop clearance momentum	Strongest mover at +6.0%/wk — protect this pace; lock in contractor capacity.

→ Continue to [03 · Zones — PoC Detail](#)

03 · Zones — PoC Detail

Detailed picture of the three PoC zones (one per geographic sub-stretch). Each contains the corridor's characteristic challenges in microcosm.

Zone	Phase	Sub-stretch	km range	Density	Daily traffic	Findings	Open
Z8	1	Port	7 – 8	High 	~96,000	8	5
Z35	3	Middle	34 – 35	High 	~134,000	9	6
Z70	5	Haram	69 – 70	High 	~178,000	9	4

Zone 8 — Port stretch

Phase 1 · port sub-stretch · workshops belt

The first concentration of distortion on the corridor. Mechanic and bodywork shops have grown organically along the right-of-way, with heavy-vehicle traffic deteriorating the asphalt and median barriers.

Findings

ID	Type	Title	Status	Severity	Owner
F-Z8-001	Dev	Demolish 14 unlicensed workshops north of carriageway	In progress	High	JM
F-Z8-002	Dev	Replace 1.2 km of damaged concrete barriers (median)	Open	High	RGA
F-Z8-003	Dev	Overlay 1.0 km asphalt — eastbound lanes	Done	Medium	RGA
F-Z8-004	Ops	Remove 6 non-compliant ad boards	In progress	Medium	JM
F-Z8-005	Ops	Fuel station signage code violation — Station #12	Open	Low	JM
F-Z8-006	Ops	Open trench left unfilled by utility contractor	Blocked	High	RGA
F-Z8-007	Ops	Recurring oil-spill from car repair yard (×3)	In progress	High	GD CD
F-Z8-008	Dev	Plant 320 native trees along north service road	Open	Low	Investment

Budget: SAR 15,450,000 committed · SAR 4,990,000 spent (~32%)

Assets in zone

- Logistics Service Center
- Fuel Station #12 (under signage review)
- Inspection Point — Port

What leadership should know

- Z8-007 is a **repeat-offender pattern** (3rd flag this quarter) — operational remediation is no longer working; needs a development-level decision (licensing review or demolition).
- Z8-006 is **blocked** by a non-responsive fiber contractor — escalation candidate for the joint working room.

Zone 35 — Middle stretch

Phase 3 · middle sub-stretch · slums, ad boards, fuel stations

The corridor's most visually disorderly stretch: a residential slum cluster south of the carriageway, a chain of oversize / mis-sized ad boards, and a fuel-station plaza non-compliant with the new urban code.

Findings

ID	Type	Title	Status	Severity	Owner
F-Z35-001	Dev	Demolish slum area (~42 condemned dwellings)	In progress	High	HCM
F-Z35-002	Dev	Re-tender ad-board concession (visual-quality plan)	Open	Medium	Investment
F-Z35-003	Dev	Rebuild Service Plaza #4 to new urban code	Open	Medium	Investment
F-Z35-004	Ops	Daily refuse pile-up at slum boundary	In progress	Medium	HCM
F-Z35-005	Ops	Two ad boards leaning post-windstorm	Done	High	HCM
F-Z35-006	Ops	Canopy paint faded — Station #18	Open	Low	HCM
F-Z35-007	Ops	Building façade graffiti (3 buildings)	In progress	Low	HCM
F-Z35-008	Ops	Pothole cluster — westbound shoulder	Open	Medium	RGA
F-Z35-009	Dev	Convert 6 ha of vacant median to landscaped strip	Open	Low	Investment

Budget: SAR 31,200,000 committed · SAR 4,200,000 spent (~13%)

Assets in zone

- Condemned dwellings cluster (slum boundary, in demolition)
- Service Plaza #4 (under rebuild)
- Median landscaping strip (planned)

What leadership should know

- **Largest development budget of any PoC zone** (SAR 31.2M), but only 13% spent — most work is at procurement / pre-mobilization stage.
- The slum demolition (F-Z35-001) is the corridor's most stakeholder-sensitive item: requires coordinated relocation with social services.

- HCM owns most of this zone's items (6 of 9) — clear single-contractor accountability.

Zone 70 — Haram approach

Phase 5 · haram sub-stretch · pilgrim entry

The most leadership-visible zone on the corridor. Welcomes pilgrims at Prince Nayef Bridge with the bridge perimeter, inspection point, and final median planting setting the **first impression of the Makkah experience**.

Findings

ID	Type	Title	Status	Severity	Owner
F-Z70-001	Dev	Restore Prince Nayef Bridge approach perimeter	In progress	High	RGA
F-Z70-002	Dev	Replace inspection-point canopy & paint	Open	High	GDT
F-Z70-003	Dev	Replace 600 m concrete barriers — bridge approach	In progress	High	RGA
F-Z70-004	Ops	Trash overflow at inspection point	In progress	Medium	HCM
F-Z70-005	Ops	Unauthorized vinyl banner on overpass railing	Open	Low	HCM
F-Z70-006	Ops	Reflective paint worn on 80 m of barriers	Open	Medium	RGA
F-Z70-007	Ops	Surface cracking — bridge expansion joint	In progress	High	RGA
F-Z70-008	Dev	Pilgrim approach landscaping — median planting	Open	Medium	Investment
F-Z70-009	Ops	Adjacent building façade obstructing welcome signage	Blocked	Medium	HCM

Budget: SAR 20,750,000 committed · SAR 5,120,000 spent (~25%)

Assets in zone

- Prince Nayef Bridge — approach (under perimeter restoration)
- Pilgrim-Approach Inspection Point
- Welcome landscaping median (planned)

What leadership should know

- **4 of 9 findings are high severity** — the densest high-severity concentration of any PoC zone.
 - Z70-009 is **blocked** waiting on a building owner to remove a façade obstruction — escalation candidate.
 - Three high-severity development items (bridge perimeter, inspection canopy, barrier replacement) **must close before Hajj 2027** to deliver the welcome experience.
-

Cross-zone summary

Metric	Z8	Z35	Z70	Total
Findings	8	9	9	26
Development	3	4	3	10
Operational	5	5	6	16
Open	5	6	4	15
Done	1	1	0	2
Blocked	1	0	1	2
High severity	4	1	4	9
Budget committed (SAR)	15.45 M	31.20 M	20.75 M	67.40 M
Budget spent (SAR)	4.99 M	4.20 M	5.12 M	14.31 M

→ Continue to [04 · Contractors & Governance](#)

04 · Contractors & Governance

Why this matters: The April 2026 report names **lack of a single supervising authority** as the *first* of four root-cause challenges. The corridor is delivered by 10 contractors — 6 government-internal teams and 4 private-sector vendors — and leadership needs a single view of who is performing, who is slipping, and who needs intervention.

The 10 contractors

Acronym	Full name (EN)	Full name (AR)	Kind	Scope
MoMAH	Ministry of Municipalities & Housing	وزارة البلديات والإسكان	Government	Governance owner, standards, policy
HCM	Holy Capital Municipality (Makkah)	أمانة العاصمة المقدسة	Government	Operates the Makkah-side stretch (in-house)
JM	Jeddah Municipality	أمانة جدة	Government	Operates the Jeddah-side stretch (in-house)
RGA	Roads General Authority	الهيئة العامة للطرق	Government	Asphalt, bridges, road safety (internal program)
GDT	General Department of Traffic	الإدارة العامة للمرور	Government	Traffic flow, inspection points
GD CD	General Directorate of Civil Defense	المديرية العامة للدفاع المدني	Government	Emergency, safety inspections
ARC	Al-Rajhi Construction Co.	شركة الراجحي للإنشاءات	Private	Heavy civil works — demolition, asphalt, barriers
SBG	Saudi Binladin Group	مجموعة بن لادن السعودية	Private	Bridge restoration, structural & pilgrim-approach
MAAS	MA'AS Services	ماس للخدمات	Private	Daily ops — refuse, signage, graffiti, ad-board take-downs
TIP	Tatweer Investment Partner	شريك تطوير الاستثمار	Private (PPP)	Ad-board concessions, fuel-station rebuild, greenery

Vendor Scorecard

Synthetic PoC data — designed to demonstrate the kind of vendor oversight leadership needs.

Contractor	Contract value (SAR)	On-time %	Quality	Fines YTD (SAR)	Late items	Escalations
MAAS	8.5 M	94%	88	25,000	0	0
HCM	9.4 M	81%	82	0	1	1
JM	6.2 M	76%	79	0	1	0
GDT	1.75 M	70%	84	0	1	0
SBG	14.8 M	71%	92	180,000	1	1
ARC	22.5 M	64%	73	450,000	2	2
RGA	11.8 M	58%	78	0	3	2
TIP	18.9 M	52%	76	320,000	3	1
GDCCD	0	100%	95	0	0	0
MoMAH	0	100%	100	0	0	0

Total corridor contract value committed: ~ SAR 93.8 M across all contractors.

What the scorecard shows

Signal	What we see
Best operational performer	MAAS — 94% on-time, near-zero fines. Protect this contract.
Highest quality	SBG — 92/100 quality (best bridge work). Trade-off: slower delivery.
Most concerning	TIP — only 52% on-time, SAR 320k fines, 3 late items on a SAR 18.9 M contract.
Most fined	ARC — SAR 450k YTD. Big contract value (22.5 M) but discipline issues.
Quietly slipping	RGA — internal team running 3 late items on barrier replacement.

Why governance is a root cause

Per the report (slide 9), corridor work today touches:

- **4 contractors** in maintenance
- **7 contractors** in infrastructure projects
- **3 contractors** in studies
- **4 contractors** (incl. private sector) in commercial / concession projects

This fragmentation creates predictable failure modes:

1. **No single owner for end-to-end outcomes.** Pilgrim-experience targets like "the corridor is clean and welcoming for Hajj" fall between RGA (road), HCM (street), GDT (traffic posts), and TIP (greenery). When something slips, accountability diffuses.
2. **Coordination tax on every multi-contractor item.** F-Z70-009 (façade obstructing welcome signage) is *blocked* because the fix requires HCM enforcement, owner notice, and possibly RGA/GDT sign-off.
3. **Duplicated studies, inconsistent standards.** Different contractors commission separate studies for adjacent assets, producing incompatible specs.
4. **No unified operational view.** Leadership cannot ask "what is the status of MBS Road this week — including vendor performance?" and get one answer.

The proposed fix — Joint Working Room

The report recommends standing up an **independent program** with three properties:

Property	Detail
Lead	MoMAH (single accountable owner)
Members	HCM (Makkah side) + JM (Jeddah side), plus standing seats for RGA, GDT, GDCCD, and the private contractors (ARC, SBG, MAAS, TIP)
Mandate	Authority over findings remediation, contractor performance review , contractor escalation, single weekly status report to leadership

Operating model: weekly cadence, shared findings backlog, vendor scorecard reviewed monthly, escalation SLA for blocked items (target: any blocked item resolved in the room ≤ 10 days).

Implication for the agent

The agent must:

- Speak **in the language of the joint room**, not in contractor silos

- For every finding, surface the **executing contractor** alongside status and severity (so leadership knows whom to call)
- Highlight **blocked items where the blocker is a contractor hand-off** (these are exactly what the room exists to resolve)
- Flag **vendors with deteriorating performance** before they become escalations

→ Continue to [05 · Activity Types & Glossary](#)

05 · Activity Types & Glossary

The two activity types

The corridor's work is organized into **two distinct activity types** with different lifecycles, owners, and budgets.

	Development Activity	Operational Activity
Source	The report's 4 root-cause findings	Day-to-day inspector findings
Cycle	Long (months to years)	Short (days to weeks)
Owner type	Capital-project teams + contractors	Field inspectors + cleaning / maintenance crews
Budget	Significant (SAR millions)	Operational ledger (no per-item budget)
Examples	New fuel station to code · workshop demolition · barrier replacement · asphalt overlay · bridge restoration · greenery program	Ad-board removal · graffiti cleanup · pothole patch · refuse collection · faded paint · signage fix
Lifecycle	Plan → Tender → Mobilize → Construct → Handover	Open → Assigned → Fixed → Verified
Linked to	Concrete capital project IDs	An inspector name + a reopened-count metric

In the corridor today: 10 Development items + 16 Operational items across the 3 PoC zones (26 total).

When operational findings escalate to development

A repeat-offender pattern signals that operational handling is insufficient. The threshold pattern:

Same finding category, same location, **reopen count > 2** → escalate to a development decision (licensing review, demolition, code-level change).

Example in PoC scope: F-Z8-007 (recurring oil-spill from a car repair yard) has reopened 3 times this quarter. The next ticket type is a development item — licensing review or workshop demolition.

Distortion categories (10)

The 10 distortion manifestations identified in the report (slide 6). Each finding is tagged with one.

Category (EN)	Category (AR)	Typical owner
Slums	عشوائيات	HCM / JM
Buildings violating urban codes	مباني غير ملتزمة بالأكواد	HCM / JM
Damaged concrete barriers	تشوه الحواجز الخرسانية	RGA
Asphalt deterioration / open trenches	تدهور الأرصفة / حفر	RGA
Bridge perimeter degradation	تدهور حرم الجسور	RGA
Fuel / service-station code violations	عدم التزام محطات الوقود	HCM / JM / Investment
Distorted ad boards	لوحات إعلانية مشوهة	HCM / JM / Investment
Unfinished construction (سواكر)	سواكر	HCM / JM
Illegal workshops & warehouses	ورش ومستودعات غير نظامية	JM / GD CD
Inspection-point appearance	مظهر نقاط التفتيش	GDT / HCM

Asset types (mapped on the corridor)

Asset (EN)	Asset (AR)	Notes
Bridge	كبري	e.g., Prince Nayef Bridge (Z70), Bahrah Bridge
Fuel station	محطة وقود	Code compliance is a recurring issue
Inspection point	نقطة تفتيش	GDT-operated, appearance matters for pilgrim welcome
Service center	مركز خدمات	Logistics / commercial cluster
Slum area	عشوائيات	Demolition + relocation lifecycle
Greenery / median strip	تشجير / جزر وسطية	The slowest-moving 2027 KPI

Glossary

Term (EN)	Term (AR)	Definition
Visual / urban distortion	تشوه بصري / حضري	Any element that degrades the visual quality of the corridor — graffiti, oversize ad boards, unfinished construction, abandoned vehicles, broken barriers, etc.
Zone	نطاق	A 1-km segment of the corridor. There are 75 zones in total (Z1–Z75). PoC data exists for Z8, Z35, Z70.
Phase	مرحلة	One of 5 operational rollout phases. Each phase covers 15 zones (15 km).
Sub-stretch	قطاع جغرافي	One of three natural geographic segments: Port (0–30 km), Middle (30–64 km), Haram (64–75 km).
Development activity	نشاط تطويري	Major capital fix — has budget, contractor, target date.
Operational activity	نشاط تشغيلي	Day-to-day inspector finding — short cycle, no major budget.
Repeat offender	مخالف متكرر	A property / asset flagged for the same finding ≥ 3 times — triggers escalation.
Blocked	متعثرة	Work that cannot progress because of an external dependency. The joint working room's first-priority queue.
Joint working room	غرفة عمل مشتركة	The proposed multi-contractor operations room led by MoMAH (with HCM + JM as core members).
Hajj-readiness	جاهزية الحج	Cumulative progress on visible items along the pilgrim approach, anchored to the next Hajj date.
PoC zone	نطاق تجريبي	One of {Z8, Z35, Z70} — zones populated with synthetic data for this proof of concept.

→ Continue to 06 · Questions & Answers

06 · Questions & Answers

62 bilingual (EN+AR) Q&A pairs the MBS Road Control Tower Agent must answer reliably. Each answer is grounded in the **Facts Snapshot** — the agent never invents numbers.

Index

#	Category	Questions
01	Corridor basics	4
02	Phases & zones	5
03	2027 targets / KPIs	8
04	Findings — status	8
05	Findings — by zone	8
06	Contractors & governance	6
07	Vendor performance	8
08	Budget	4
09	Hajj readiness	4
10	Activity types	4
11	Scope & safety	3

1. Corridor basics

أساسيات المحور

C-01 How long is the MBS Road corridor and where does it run?

ما طول محور طريق الأمير محمد بن سلمان وأين يمتد؟

Answer (EN): 75 km from Jeddah Islamic Port to Al-Masjid Al-Haram in Makkah.

Answer (AR): 75 كم من ميناء جدة الإسلامي إلى المسجد الحرام في مكة المكرمة.

C-02 How many vehicles use the road every day?

كم عدد المركبات التي تستخدم الطريق يومياً؟

Answer (EN): More than 170,000 vehicles daily.

Answer (AR): أكثر من 170,000 مركبة يومياً.

C-03 Why is this corridor strategically important?

لماذا يُعد هذا المحور استراتيجياً؟

Answer (EN): It is the principal connection between Jeddah and Makkah and the main road used by pilgrims and Umrah travellers to reach Al-Masjid Al-Haram, as well as a logistics spine from the Islamic Port.

Answer (AR): يمثل الرابط الرئيسي بين جدة ومكة والطريق الأساسي الذي يستخدمه الحجاج والمعتزمون للوصول إلى المسجد الحرام، فضلاً عن كونه عموداً فقرياً للوجستيات من الميناء الإسلامي.

C-04 What are the three geographic sub-stretches of the road?

ما القطاعات الجغرافية الثلاثة للطريق؟

Answer (EN): Port → Bahrah (0–30 km, logistics & workshops), Bahrah → Prince Nayef (30–64 km, inter-city / fuel / ad-boards / slum pockets), and Prince Nayef → Holy Mosque (64–75 km, pilgrim approach).

Answer (AR): الميناء → بحرة (0–30 كم، لوجستيات وورش)، بحرة → الأمير نايف (30–64 كم، نقل بين مدن / محطات وقود / لوحات / عشوائيات)، الأمير نايف → الحرم (64–75 كم، مدخل الحجاج).

2. Phases & zones

المراحل والنطاقات

S-01 How is the corridor broken down into phases and zones?

كيف يُقسَّم المحور إلى مراحل ونطاقات؟

Answer (EN): 5 rollout phases, each covering 15 zones of 1 km — 75 zones in total. Phase 1: Z1–Z15, Phase 2: Z16–Z30, Phase 3: Z31–Z45, Phase 4: Z46–Z60, Phase 5: Z61–Z75.

Answer (AR): المرحلة 1: Z1–Z15، المرحلة 2: Z16–Z30، المرحلة 3: Z31–Z45، المرحلة 4: Z46–Z60، المرحلة 5: Z61–Z75. إجمالي 75 نطاقاً من كم — المرحلة 1: 5.

S-02 Which zones are part of the proof-of-concept?

ما النطاقات المشمولة في المرحلة التجريبية؟

Answer (EN): Three zones: Z8 (port stretch — workshops belt), Z35 (middle stretch — slum + ad-board cluster), Z70 (Haram approach — bridge perimeter & pilgrim entry).

Answer (AR): ثلاثة نطاقات: Z8 (قطاع الميناء — حزام ورش)، Z35 (القطاع الأوسط — عشوائيات ولوحات)، Z70 (مدخل الحرم — حرم الكبرى ومدخل الحجاج).

S-03 What is the difference between a phase and a sub-stretch?

ما الفرق بين المرحلة والقطاع الجغرافي؟

Answer (EN): A phase is an operational rollout slice (when work is scheduled). A sub-stretch is a geographic character (port-logistics vs middle vs Haram approach). Every zone carries both labels.

Answer (AR): المرحلة شريحة إطلاق تشغيلية (متى سَيُنقَذ العمل). القطاع الجغرافي يصف طبيعة الموقع (ميناء / لوجستيات / وسط / مدخل الحرم). كل نطاق يحمل التصنيفين معاً.

S-04 Which phase does Zone 70 belong to?

إلى أي مرحلة ينتمي النطاق 70؟

Answer (EN): Phase 5 (Z61–Z75), sub-stretch 'Prince Nayef → Holy Mosque'.

Answer (AR): 'القطاع' الأمير نايف → الحرم، (Z61–Z75) المرحلة 5.

S-05 What distortion-density bands are used on the map?

ما تصنيفات كثافة التشوه المستخدمة على الخريطة؟

Answer (EN): Three: low (green), medium (orange), high (red). Each 1 km zone is colored by its current band.

Answer (AR): ثلاثة: منخفضة (أخضر)، متوسطة (برتقالي)، عالية (أحمر). كل نطاق طوله 1 كم يُلون بحسب تصنيفه الحالي.

3. 2027 targets / KPIs

مستهدفات 2027

K-01 How many 2027 targets are we tracking?

كم عدد مستهدفات 2027 التي نتابعها؟

Answer (EN): Six: road maintenance coverage, building compliance, illegal-workshop removal, barrier repair, condemned-building demolition, greenery & median planting.

Answer (AR): ستة: تغطية الصيانة، امتثال المباني، إزالة الورش غير النظامية، إصلاح الحواجز، هدم المباني الملغاة، التشجير والجزر الوسطية.

K-02 What is the road-maintenance coverage target and where are we?

ما مستهدف تغطية صيانة الطريق وأين وصلنا؟

Answer (EN): Target is 100% coverage by end of 2027. We are at 38% currently, trending +4.2% per week.

Answer (AR): المستهدف 100% تغطية بحلول نهاية 2027. الوضع الحالي 38%، باتجاه +4.2% أسبوعياً.

K-03 How are we doing on barrier-repair progress?

ما تقدّمنا في إصلاح الحواجز الخرسانية؟

Answer (EN): Target: 90% repaired by 2027 end. Current: 53% (+5.3% weekly).

Answer (AR): المستهدف: إصلاح 90% بنهاية 2027. الحالي: 53% (+5.3% أسبوعياً).

K-04 Which KPI is furthest behind?

أي مستهدف هو الأكثر تأخراً؟

Answer (EN): Greenery & median planting — only 19% of the 100% target so far, growing slowly at +1.4% per week.

Answer (AR): التشجير والجزر الوسطية — 19% فقط من المستهدف 100%، ينمو ببطء بمعدل +1.4% أسبوعياً.

K-05 Which KPI is most on track?

أي مستهدف هو الأقرب للمسار المخطط؟

Answer (EN): Damaged-barrier repair — 53% of a 90% target (≈59% of target) — the leading indicator.

Answer (AR): إصلاح الحواجز — 53% من مستهدف 90% (≈59% من المستهدف) — أعلى نسبة تحقيق.

K-06 What is the building-compliance target?

ما مستهدف امتثال المباني؟

Answer (EN): 70% of buildings on the corridor compliant with the unified urban code by 2027 end. Currently at 22% (+2.1% weekly).

Answer (AR): 70% %2.1+) %22 الحالي 2027. الموحد بنهاية العمراني للكود الممثلة للمحور من المباني على المحور ممتثلة للكود العمراني الموحد بنهاية 2027. الحالي 2.1+ %22 %70 (أسبوعياً).

K-07 How many condemned buildings still need to be demolished?

كم مبنى ملغى الصك ما زال يحتاج للهدم؟

Answer (EN): We are at 28% of the 100% demolition target — about 72 percentage points remaining (proportional to the corridor’s total condemned-building inventory).

Answer (AR): وصلنا إلى 28% من مستهدف الهدم البالغ 100% – يتبقى نحو 72 نقطة مئوية (متناسبة مع مجموع المباني الملغاة على المحور).

K-08 What is the workshop-clearance target?

ما تستهدف إزالة الورش غير النظامية؟

Answer (EN): 100% of illegal workshops & warehouses cleared by 2027 end. At 41% so far, +6.0% per week — strongest weekly delta.

Answer (AR): إزالة 100% من الورش والمستودعات غير النظامية بنهاية 2027. الحالي 41%، +6.0% أسبوعياً — أعلى نسبة تغيّر أسبوعي.

4. Findings — status

الملاحظات – الحالة

F-01 How many open findings are there in the PoC scope?

كم عدد الملاحظات المفتوحة ضمن نطاق التجربة؟

Answer (EN): Refer to findings_aggregate.open + in_progress + blocked counts.

Answer (AR): يُرجى الاطلاع على findings_aggregate.open + in_progress + blocked.

F-02 What is our overall closure rate?

ما معدل الإغلاق الإجمالي؟

Answer (EN): Computed as done / total. See findings_aggregate.done and findings_aggregate.total.

Answer (AR): done / total. findings_aggregate.done و findings_aggregate.total. يُحسب بـ

F-03 How many findings are currently blocked?

كم ملاحظة متعثرة حالياً؟

Answer (EN): See findings_aggregate.blocked. Each blocked item needs escalation in the joint working room.

Answer (AR): كل بند متعثر يحتاج تصعيد في غرفة العمل المشتركة. انظر findings_aggregate.blocked.

F-04 Which high-severity findings are still open?

ما الملاحظات عالية الخطورة ولا زالت مفتوحة؟

Answer (EN): List from findings_aggregate.top_blockers (or filter all findings where severity=high and status≠done).

Answer (AR): severity=high أو رشح كل الملاحظات بـ findings_aggregate.top_blockers انظر القائمة في (status≠done).

F-05 Which distortion category has the most findings?

أي تصنيف للتشوه يحوي أكثر عدد من الملاحظات؟

Answer (EN): See findings_aggregate.by_category (largest entry).

Answer (AR): (أكبر إدخال) انظر findings_aggregate.by_category.

F-06 Which finding is closest to its deadline?

أي ملاحظة هي الأقرب لتاريخ موعدها المستهدف؟

Answer (EN): See findings_aggregate.top_blockers — the list is sorted by earliest target_date.

Answer (AR): القائمة مرتبة بالأقرب موعداً — findings_aggregate.top_blockers انظر.

F-07 How many findings have been reopened more than once?

كم ملاحظة أُعيد فتحها أكثر من مرة؟

Answer (EN): Filter findings where reopenedCount > 1 — these indicate the same issue recurring (repeat-offender pattern).

Answer (AR): هذه مؤشر على تكرار نفس المشكلة (نمط مخالف متكرر) — reopenedCount > 1 رشح الملاحظات التي.

F-08 What does 'blocked' status mean operationally?

ماذا يعني وصف 'متعثرة' تشغيلياً؟

Answer (EN): Work that cannot progress because of an external dependency (e.g., utility contractor not responding, owner notice unresolved, agency hand-off pending). These are the items the joint working room escalates first.

Answer (AR): أعمال لا يمكن تقدّمها بسبب اعتماد خارجي (مثل: مقاول مرافق غير مستجيب، إنذار مالك لم يُحل، انتقال صلاحيات بين الجهات معلق). هذه أولى البنود في غرفة العمل المشتركة للتصعيد.

5. Findings — by zone

الملاحظات — حسب النطاق

Z-01 What is the situation in Zone 8?

ما الوضع في النطاق 8؟

Answer (EN): Phase 1, port stretch, high distortion density. Workshops belt with damaged median barriers and asphalt deterioration. Multiple agencies involved (JM, RGA, GDCC, Investment).

Answer (AR): المرحلة 1، قطاع الميناء، كثافة تشوه عالية. حزام ورش مع حواجز جزيرة وسطية متهاكة وتدهور سفلتة. عدة جهات مشاركة (JM, RGA, GDCC, Investment).

Z-02 What is the situation in Zone 35?

ما الوضع في النطاق 35؟

Answer (EN): Phase 3, middle stretch, high distortion density. Slum cluster (~42 condemned dwellings), distorted ad-board cluster, fuel-station code violations. Owned mostly by HCM and the Investment partner.

Answer (AR): المرحلة 3، القطاع الأوسط، كثافة تشوه عالية. تجمع عشوائيات (~42 مسكن ملغى)، فوضى لوحات إعلانية، وشريك الاستثمار HCM مخالفات محطات وقود. مملوك غالباً لـ

Z-03 What is the situation in Zone 70?

ما الوضع في النطاق 70؟

Answer (EN): Phase 5, Haram approach, high distortion density. Prince Nayef Bridge perimeter restoration, inspection-point upgrade, barrier replacement. Highest leadership scrutiny before Hajj.

Answer (AR): المرحلة 5، مدخل الحرم، كثافة تشوه عالية. إعادة تأهيل حرم كبري الأمير نايف، تطوير نقطة التفتيش، استبدال الحواجز. أعلى تدقيق قيادي قبل الحج.

Z-04 How many findings does Zone 8 have and how many are open?

كم عدد ملاحظات النطاق 8 وكم منها مفتوحة؟

Answer (EN): Use poc_zones[id=8].findings_total and findings_open.

Answer (AR): استخدم poc_zones[id=8].findings_total و findings_open.

Z-05 Which PoC zone has the highest number of high-severity findings?

أي نطاق تجريبي يحوي أكثر ملاحظات عالية الخطورة؟

Answer (EN): Compare poc_zones[*].findings_high_severity.

Answer (AR): قارن poc_zones[*].findings_high_severity.

Z-06 Are there bridges in any PoC zone?

هل توجد كباري في أي نطاق تجريبي؟

Answer (EN): Yes — Zone 70 contains Prince Nayef Bridge (approach). Asset type 'bridge' also appears in poc_zones[id=70].asset_count_by_type.

Answer (AR): يظهر أيضاً في 'bridge' نعم — النطاق 70 يحوي كبري الأمير نايف (المدخل). نوع الأصل poc_zones[id=70].asset_count_by_type.

Z-07 What can you tell me about Zone 50?

ماذا يمكنك إخباري عن النطاق 50؟

Answer (EN): Zone 50 is in Phase 4 (Z46–Z60), middle sub-stretch. PoC data has not been injected for it yet — return the scope_notes.out_of_scope_response.

Answer (AR): القطاع الأوسط. لم تُحقن بيانات تجريبية له بعد — أعد الإجابة (Z46–Z60) النطاق 50 ضمن المرحلة 4 scope_notes.out_of_scope_response.

Z-08 Which assets are in Zone 35?

ما الأصول الموجودة في النطاق 35؟

Answer (EN): Slum-area boundary, Service Plaza #4 (fuel station), and a planned median-landscaping strip. See poc_zones[id=35].asset_count_by_type.

Answer (AR): حدود منطقة عشوائيات، مجمع الخدمة رقم 4 (وقود)، وشريط تنسيق وسطي مخطط. انظر poc_zones[id=35].asset_count_by_type.

6. Contractors & governance

المقاولون والحوكمة

A-01 Which contractors are involved on the MBS Road?

أي مقاولين يعملون على محور طريق الأمير محمد بن سلمان؟

Answer (EN): Ten in total: six government-internal entities (MoMAH — governance owner, HCM, JM, RGA, GDT, GDCCD) and four private-sector vendors (Al-Rajhi Construction — ARC, Saudi Binladin Group — SBG, MA'AS Services — MAAS, and Tatweer Investment Partner — TIP).

Answer (AR): عشرة إجمالاً: ستة جهات حكومية داخلية (MoMAH — مالكة الحوكمة، HCM، JM، RGA، GDT، GDCCD) وأربعة مقاولين من القطاع الخاص (شركة الراجحي للإنشاءات — ARC، مجموعة بن لادن السعودية — SBG، ماس — MAAS، وشريك تطوير الاستثمار — TIP).

A-02 Which contractor owns the most findings overall?

أي مقاول يحمل أكبر عدد من الملاحظات؟

Answer (EN): Take the largest entry of findings_aggregate.by_contractor — currently TIP and MAAS share the lead with 5 each, followed by ARC at 4.

Answer (AR): يتشاركان الصدارة بـ MAAS و TIP حالياً — findings_aggregate.by_contractor انظر أكبر إدخال في بـ 4 ARC 5 ملاحظات لكل منهما، يليهما.

A-03 Which contractor has the most blocked items?

أي مقاول لديه أكثر بنود متعثرة؟

Answer (EN): Compare contractors[*].blocked_findings_count and take the max — currently RGA and HCM each have 1 blocked item open.

Answer (AR): لدى كل منهما بند متعثر HCM و RGA حالياً — contractors[*].blocked_findings_count قارن واحد مفتوح.

A-04 Why does the report say governance is one of the four root causes?

لماذا يقول التقرير إن الحوكمة هي أحد الأسباب الجذرية الأربعة؟

Answer (EN): Because no single authority oversees the corridor end-to-end — 4 contractors involved in maintenance, 7 in infrastructure projects, 3 in studies, 4 in private-sector projects. Roles overlap and there is no joint operations room (slide 9).

Answer (AR): لأنه لا توجد جهة واحدة مشرفة على المحور كاملاً — 4 مقاولين في الصيانة، 7 في البنية التحتية، 3 في الدراسات، 4 في القطاع الخاص. تتداخل الأدوار ولا توجد غرفة عمليات مشتركة (شريحة 9).

A-05 What is the proposed governance fix?

ما الحل الحوكمي المقترح؟

Answer (EN): An independent program led by MoMAH that joins HCM (Makkah) and Jeddah Municipality in a shared working room with mandates for findings remediation, vendor performance oversight, and stakeholder coordination.

Answer (AR): وأمانة جدة في غرفة عمل مشتركة بصلاحيات معالجة (مكة) HCM يجمع MoMAH برنامج مستقل بقيادة الملاحظات، ومتابعة أداء المقاولين، وتنسيق أصحاب المصلحة.

A-06 Who is responsible for greenery and ad-board concessions?

من المسؤول عن التشجير وامتيازات اللوحات الاعلانية؟

Answer (EN): Tatweer Investment Partner (TIP) — a PPP vendor — under MoMAH oversight.

Answer (AR): MoMAH. مقاول شراكة بين القطاعين العام والخاص — تحت إشراف — (TIP) شريك تطوير الاستثمار.

7. Vendor performance

أداء المقاولين

V-01 Who is our best-performing vendor overall?

من هو أفضل مقاول من حيث الأداء بشكل عام؟

Answer (EN): Use vendor_performance.best_overall — based on a composite score that weights on-time delivery (40%), quality (30%), low fines (20%), and few late items (10%).

Answer (AR): مبني على نتيجة مركبة تزن الالتزام بالمواعيد (40%)، — vendor_performance.best_overall انظر — الجودة (30%)، انخفاض الغرامات (20%)، وقلة البنود المتأخرة (10%).

V-02 Which vendor has the most fines this year?

أي مقاول لديه أكبر مبلغ غرامات هذا العام؟

Answer (EN): Use vendor_performance.most_fined — Al-Rajhi Construction (ARC) leads at SAR 450,000 YTD, followed by Tatweer Investment Partner (TIP) at SAR 320,000.

Answer (AR): في المقدمة بـ (ARC) شركة الراجحي للإنشاءات — vendor_performance.most_fined انظر — بـ 320,000 ر.س (TIP) 450,000 ر.س منذ بداية العام، يليها شريك تطوير الاستثمار.

V-03 Which vendor is slipping on deadlines / has the most late findings?

أي مقاول متأخر عن المواعيد / لديه أكثر بنود متأخرة؟

Answer (EN): Use vendor_performance.most_late — Tatweer Investment Partner (TIP) currently has the most late findings (3), followed by RGA (3) and ARC (2).

Answer (AR): انظر vendor_performance.most_late — لديه أكثر بنود متأخرة (3)، (TIP) شريك تطوير الاستثمار — vendor_performance.most_late انظر (2). RGA (3) يليه ARC (2).

V-04 Which vendor delivers the highest quality?

أي مقاول يقدم أعلى مستوى جودة؟

Answer (EN): Use vendor_performance.highest_quality — Saudi Binladin Group (SBG) leads with a quality score of 92/100. They are slower on deadlines but their bridge work meets the highest spec.

Answer (AR): انظر vendor_performance.highest_quality — مجموعة بن لادن السعودية (SBG) في المقدمة بنتيجة جودة 92/100. أبطأ في المواعيد لكن أعمال الكباري لديها وفق أعلى مواصفات.

V-05 Who holds the largest contract on the corridor?

أي مقاول لديه أكبر قيمة عقد على المحور؟

Answer (EN): Use vendor_performance.largest_contract — Al-Rajhi Construction (ARC) at SAR 22.5M, followed by Tatweer Investment Partner (TIP) at SAR 18.9M and Saudi Binladin Group (SBG) at SAR 14.8M.

Answer (AR): انظر vendor_performance.largest_contract — شركة الراجحي للإنشاءات (ARC) بقيمة 22.5 مليون ر.س، ثم مجموعة بن لادن السعودية (TIP) 18.9 مليون ر.س، يليها شريك تطوير الاستثمار (SBG) 14.8 مليون ر.س.

V-06 What is the total contract value committed on the corridor across all vendors?

ما إجمالي قيمة العقود الملتزم بها على المحور لدى جميع المقاولين؟

Answer (EN): Use vendor_performance.total_corridor_contract_value_sar.

Answer (AR): انظر vendor_performance.total_corridor_contract_value_sar.

V-07 Show me the full vendor scorecard ranking.

أعرض بطاقة أداء كل المقاولين مرتبة.

Answer (EN): Use vendor_performance.ranked_by_composite — vendors sorted by composite score (best first). Each entry has the contractor's id, acronym, and composite score (0..100).

Answer (AR): انظر vendor_performance.ranked_by_composite — مقاولون مرتبون حسب النتيجة المركبة (الأفضل أولاً). كل إدخال يحوي المعرف والاختصار والنتيجة المركبة (100..0).

V-08 Which vendor should we be most concerned about and why?

أي مقاول يجب أن نقلق منه أكثر ولماذا؟

Answer (EN): Tatweer Investment Partner (TIP) — lowest on-time rate among active vendors (52%), 3 late findings, SAR 320,000 in fines YTD, and 1 escalation. Combined with their large SAR 18.9M contract, this exposure warrants leadership attention. Action: schedule a contractor performance review and consider escalation in the joint working room.

Answer (AR): أدنى نسبة التزام بالمواعيد بين المقاولين الفعّالين (52%)، 3 بنود (TIP) شريك تطوير الاستثمار متأخرة، 320,000 ر.س غرامات منذ بداية العام، وحالة تصعيد واحدة. مع حجم العقد الكبير (18.9 مليون ر.س)، هذه المخاطر تستحق اهتمام القيادة. الإجراء: جدولة مراجعة أداء المقاول ودراسة التصعيد في غرفة العمل المشتركة.

8. Budget

الميزانية

B-01 How much development budget is committed in Zone 8?

كم حجم ميزانية التطوير الملتزم بها في النطاق 8؟

Answer (EN): See poc_zones[id=8].budget_committed_sar (SAR).

Answer (AR): انظر poc_zones[id=8].budget_committed_sar (ر.س).

B-02 What share of the Zone 8 budget has been spent?

ما نسبة الإنفاق من ميزانية النطاق 8؟

Answer (EN): Compute poc_zones[id=8].budget_spent_sar / budget_committed_sar.

Answer (AR): احسب poc_zones[id=8].budget_spent_sar / budget_committed_sar.

B-03 Which PoC zone has the largest committed budget?

أي نطاق تجريبي لديه أكبر ميزانية ملتزمة؟

Answer (EN): Compare poc_zones[*].budget_committed_sar.

Answer (AR): قارن poc_zones[*].budget_committed_sar.

B-04 What is the total committed development budget across all PoC zones?

ما إجمالي ميزانية التطوير الملتزم بها لكل نطاقات التجربة؟

Answer (EN): Sum of poc_zones[*].budget_committed_sar.

Answer (AR): مجموع poc_zones[*].budget_committed_sar.

9. Hajj readiness

جاهزية الحج

H-01 How many days until the next Hajj season?

كم يوماً متبقياً حتى موسم الحج القادم؟

Answer (EN): See hajj_readiness.days_remaining and hajj_readiness.next_hajj_date.

Answer (AR): انظر hajj_readiness.days_remaining و hajj_readiness.next_hajj_date.

H-02 Are we on track for Hajj?

هل نحن ضمن المسار المخطط للحج؟

Answer (EN): Return hajj_readiness.summary_en / summary_ar — derived from average KPI progress vs target.

Answer (AR): مشتق من متوسط تقدّم المستهدفات — hajj_readiness.summary_en / summary_ar أعد

H-03 What short-term work must be done before Hajj?

ما الأعمال قصيرة المدى التي يجب إنجازها قبل الحج؟

Answer (EN): Per the report (slide 12): intensify contractor oversight, clear illegal workshops & yards, fix concrete barriers, improve appearance of inspection points along the corridor.

Answer (AR): حسب التقرير (شريحة 12): تكثيف الرقابة على المقاولين، إزالة الورش والمستودعات غير النظامية، إصلاح الحواجز الخرسانية، تحسين مظهر نقاط التفتيش على امتداد المحور.

H-04 Which zone is the highest priority for Hajj readiness?

أي نطاق له أعلى أولوية لجاهزية الحج؟

Answer (EN): Zone 70 — Prince Nayef Bridge approach is the pilgrim entry; bridge perimeter and inspection-point appearance directly shape the welcome experience.

Answer (AR): النطاق 70 — مدخل كبري الأمير نايف هو مدخل الحجاج؛ حرم الكبري ومظهر نقطة التفتيش يحددان مباشرة تجربة الترحيب.

10. Activity types

أنواع الأنشطة

T-01 What is a 'development activity'?

ما هو 'النشاط التطويري'؟

Answer (EN): Major capital fixes from the report's primary findings — e.g., new fuel station, demolish workshops, replace barriers, bridge restoration. Has a budget, contractor, target date.

Answer (AR): أعمال رأسمالية كبيرة من الملاحظات الأساسية في التقرير — مثل: محطة وقود جديدة، هدم ورش، استبدال حواجز، تأهيل كبري. لها ميزانية، مقاول، تاريخ مستهدف.

T-02 What is an 'operational activity'?

ما هو 'النشاط التشغيلي'؟

Answer (EN): Day-to-day inspector findings — mostly visual-distortion items. Short cycle (Open → Assigned → Fixed → Verified). No major budget; has an inspector name and may have a reopen count.

Answer (AR): ملاحظات مفتشين يومية — معظمها تشوه بصري. دورة قصيرة (مفتوحة → مُسندة → مُصلحة → مُتحقق منها). بلا ميزانية كبيرة؛ لها اسم مفتش وقد يكون لها عدد مرات إعادة فتح.

T-03 How many development vs operational items are tracked?

كم عدد البنود التطويرية مقابل التشغيلية؟

Answer (EN): See findings_aggregate.by_activity_type.

Answer (AR): انظر findings_aggregate.by_activity_type.

T-04 When an operational finding keeps recurring (same workshop oil-spill 3rd time), what does that mean?

إذا تكررت ملاحظة تشغيلية (نفس ورشة تسرب الزيت للمرة الثالثة)، ماذا يعني ذلك؟

Answer (EN): It is a 'repeat-offender' pattern. The reopenedCount metric flags it. These cases typically need escalation from operational handling to a development-style decision (e.g., demolition or licensing review).

Answer (AR): يرصده. تحتاج هذه الحالات عادةً للتصعيد من reopenedCount هذا نمط 'مخالف متكرر'. مؤشّر المعالجة التشغيلية إلى قرار تطويري (مثل: هدم أو مراجعة ترخيص).

11. Scope & safety

النطاق والسلامة

X-01 Can you answer questions about Riyadh roads or other cities?

هل تستطيع الإجابة عن طرق الرياض أو مدن أخرى؟

Answer (EN): No — this agent is scoped to the MBS Road corridor (Jeddah → Makkah) in the Makkah region. Anything outside that scope, decline politely and remind the user of the corridor.

Answer (AR): لا — هذا الوكيل محصور بمحور طريق الأمير محمد بن سلمان (جدة → مكة) في منطقة مكة المكرمة. أي طلب خارج هذا النطاق، اعتذر بأدب وذكّر المستخدم بنطاق المحور.

X-02 Do you have data for zones outside Z8, Z35, Z70?

هل توجد بيانات لنطاقات خارج Z8 و Z35 و Z70؟

Answer (EN): Not yet. Return `scope_notes.out_of_scope_response` and offer the zone's phase + sub-stretch if asked.

Answer (AR): واعرض المرحلة والقطاع الجغرافي إذا طُلب `scope_notes.out_of_scope_response` ليس بعد. أعد

X-03 Is the data in this PoC real?

هل البيانات في هذه التجربة حقيقية؟

Answer (EN): No — all findings, budgets, inspector names, and KPI percentages are synthetic, generated to demonstrate the platform. Real data will be loaded after sign-off.

Answer (AR): لا — جميع الملاحظات والميزانيات وأسماء المفتشين ونسب المستهدفات بيانات تجريبية أُنشئت لعرض المنصة. ستُحمّل البيانات الحقيقية بعد الاعتماد.

→ Continue to 07 · Facts Snapshot (JSON)
